MAISON LUMEN · ORACLE EPM ROLLOUT

Project Initiation Documentation

Lumen Rollout: deploying Oracle EPM Planning (EPBCS) and Financial Consolidation (FCCS)

Project	Lumen Rollout · Maison Lumen Group
Document	LR-PID-001 · version 1.0 · approved
Date	27 March 2026 (charter approval, milestone M1)
Prepared by	Gaurav Sharma, project manager
Approved by	Marc Dubois, CFO and project executive

Portfolio sample. Maison Lumen, its people and all figures are fictional. PRINCE2® is a registered trademark of PeopleCert; Oracle, EPBCS and FCCS are trademarks of Oracle Corporation. Not affiliated with either.

Document control

Document ID	LR-PID-001
Status	Approved by the steering committee on 27 March 2026 (decision DC1)
Purpose	Defines the project so the steering committee can authorise it and use it as the baseline for all later decisions
Related documents	Solution design documents (LR-DES-EPBCS-001, LR-DES-FCCS-001) · Project control workbook (RAID log, change log, UAT test plan, go/no-go checklist)

Version history

Version	Date	Author	Changes
0.1	13 Mar 2026	G. Sharma	First draft after the kick-off
0.4	20 Mar 2026	G. Sharma	Business case figures from finance; tolerances proposed
1.0	27 Mar 2026	G. Sharma	Approved at the steering committee (milestone M1)

Approval

Project board role	Name	Position	Decision
Executive (sponsor)	Marc Dubois	Chief financial officer	**Approved**
Senior user, planning	Claire Martin	Paris site controller, FP&A key user	Reviewed
Senior user, consolidation	Sophie Bernard	Head-office and group controller	Reviewed
Senior supplier	Nicolas Petit	IT and ERP lead	Reviewed

Contents

1. Background
2. Project definition
3. Business case summary
4. Project approach
5. Organisation
6. Plan summary
7. Tolerances
8. Project controls
9. Risk management approach
10. Quality management approach
11. Communication plan

1. Background

Maison Lumen is a French lighting manufacturer with a head office in Lyon, a sales site in Paris, a plant in Lille and subsidiaries in the United Kingdom, the United States (80 % owned) and India. Its budget and forecast run on about forty linked Excel files, and the group consolidation on a spreadsheet model maintained by one person.

Last year the budget took ten weeks, the monthly forecast a full week, and the half-year consolidation closed at day 12 after two late intercompany corrections. The auditors asked for a traceable consolidation process. The CFO decided to replace both processes with Oracle EPM Cloud before the FY27 budget and the FY26 year-end close.

2. Project definition

2.1 Objectives

Objective	Measure	Target
Launch the FY27 budget in Oracle EPM Planning	EPBCS in production	2 November 2026
Shorten the budget cycle	Weeks from launch to approval	6 weeks (10 today)
Shorten the monthly forecast	Working days to update the forecast	3 days (7 today)
Close the FY26 year-end consolidation in FCCS	FCCS in production	8 January 2027
Close the consolidation faster	Working days after month end	Day 8 (day 12 today)
Deliver within budget	Cost at completion	480 k€ (+5 % tolerance)

2.2 Scope

In scope	Out of scope
Oracle EPM Planning (EPBCS): forecast and budget of the French sites	Workforce planning by employee
Oracle FCCS: consolidation of the four group companies, IAS 21 translation, eliminations, NCI	Capital expenditure and cash-flow planning
Monthly ERP data flows for actuals and trial balances	Narrative Reporting (management packs)
Reports, security, testing, training and hypercare	ERP changes other than the extracts

2.3 Deliverables

Deliverable	Accepted by	Acceptance
Solution design documents (EPBCS, FCCS)	Senior users	Design sign-off (M2)
Configured EPBCS and FCCS applications	Senior users	UAT exit criteria met
ERP data flows with mapping and reconciliation	IT and ERP lead	Monthly load reconciled
Reports and security by entity	Senior users	UAT cases passed
User guides and training	Senior users	90 % of users trained

Deliverable	Accepted by	Acceptance
Handover to support	IT and ERP lead	Support procedure tested

2.4 Constraints, assumptions and dependencies

- **Constraint.** EPBCS must be live before the FY27 budget launch; FCCS must be proven on a real close before the year end.
- **Constraint.** Key users are busy in October and November with the budget season.
- **Assumption AS1.** Key users give two half-days a week to testing.
- **Assumption AS2.** The group chart of accounts stays frozen until the FCCS go-live.
- **Assumption AS3.** Existing Oracle EPM licences cover 60 users at no extra cost.
- **Assumption AS4.** The 2024–2025 history can be extracted from the ERP without rework.
- **Dependencies.** ERP team for the data flows; Oracle's monthly updates; treasury for closing exchange rates.

3. Business case summary

Option	Description	Assessment
1. Do nothing	Keep the Excel models	Rejected: cycle times and audit findings remain
2. Improve Excel	Rebuild the models with controls and macros	Rejected: still manual, depends on key people
3. Oracle EPM Cloud	EPBCS for planning, FCCS for consolidation	**Recommended**: standard processes, audit trail, faster cycles

Item	Value
Project budget	480 k€ (integrator and internal time), excluding licences already in the IT run budget
Contingency	48 k€ (10 %), held by the sponsor and released through change control
Timescale	2 March 2026 to 22 January 2027
Expected benefits	Budget in 6 weeks instead of 10; forecast in 3 days instead of 7; consolidation at day 8 instead of day 12; about 1.5 FTE of finance time freed for analysis
Main risks	Quality of ERP history (R1), key-user availability (R2), late ERP flows (R3)

Benefits review

The sponsor reviews the benefits after the first FY27 budget cycle and the first FCCS year-end close, using the measures in section 2.1.

4. Project approach

The project follows a hybrid approach, common for EPM implementations: sequential stages each closed by a steering committee decision, with the build delivered as three conference room pilots (CRPs) reviewed with key users. Configuration starts from Oracle's standard features and adds only what a documented requirement justifies.

- **Environments.** One test and one production environment per application; Oracle updates test on the first Friday of each month and production on the third, so regression tests run in between.
- **Team.** Integrator consultants build; internal key users design, test and become the application owners.
- **Knowledge transfer.** Every configuration is documented and paired with an internal owner (risk R6).

5. Organisation

Role	Name	Responsibilities
Project executive (sponsor)	Marc Dubois, CFO	Owns the business case; chairs the steering committee; releases contingency
Senior users	Claire Martin, Sophie Bernard	Represent planning and consolidation users; accept the deliverables
Senior supplier	Nicolas Petit, IT and ERP	Commits IT and integrator resources; owns the data flows
Project manager	Gaurav Sharma	Plans and runs the project day to day, within the tolerances set by the board
EPM consultants	Integrator team	Design, build, testing support, training
Key users	FP&A and consolidation teams	Workshops, test cases, UAT, champions in each entity
Auditors (consulted)	Statutory auditors	Review of consolidation rules before go-live

RACI for key activities

Activity	Sponsor	PM	Consultant	Key users	Consol.	IT	Auditors
Approve business case and charter	A	R	C	I	I	C	
Run design workshops		A	R	C	C	I	
Sign off the design	A	R	C	C	C	I	
Build EPBCS and FCCS		A	R	C	C		
Build the ERP data flows		A	C			R	
Validate consolidation rules	C	I	R		A		C
Write and run test cases		A	C	R	R		
Train users		A	R	C	C		
Decide go/no-go	A	R	C	C	C	C	I

6. Plan summary

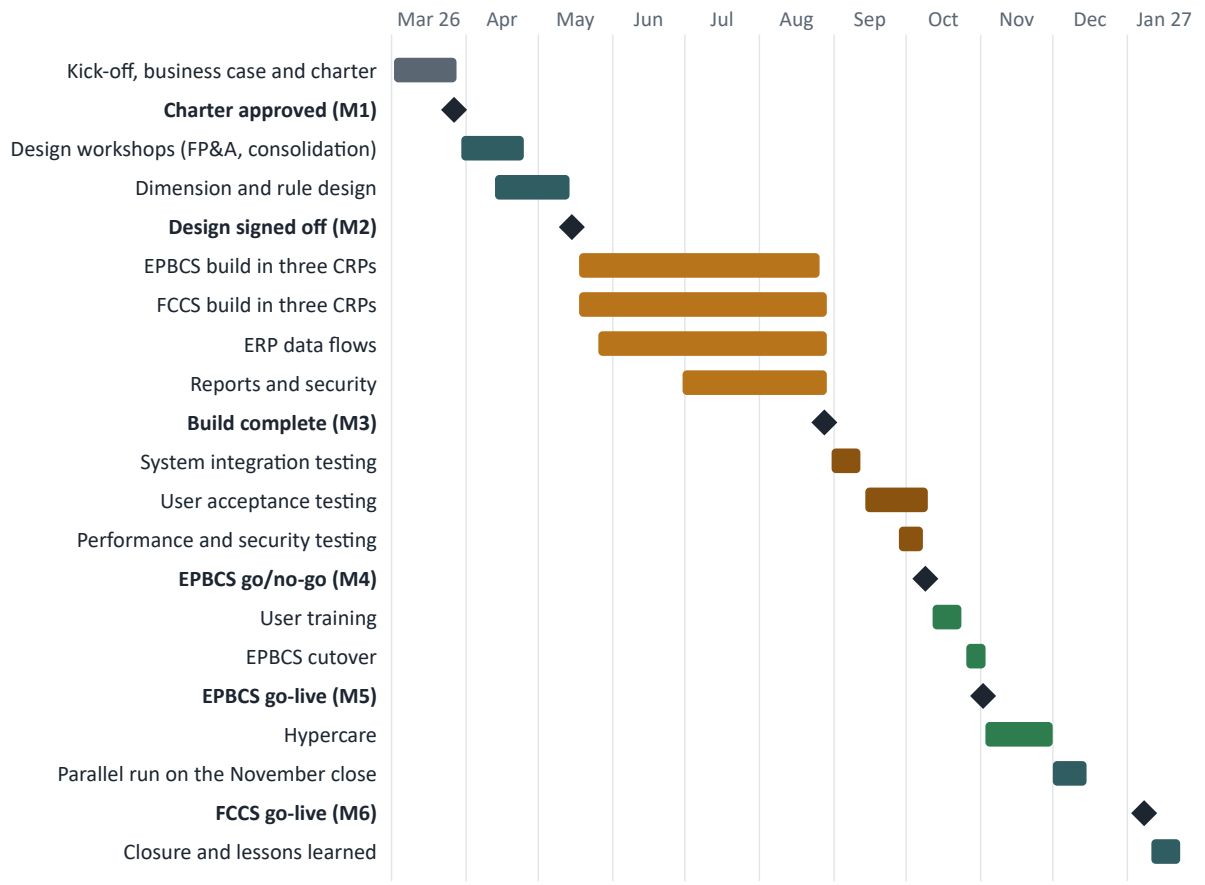


Figure 1. Baseline plan, in working days (weekends and French public holidays excluded)

Milestone	Baseline date	Decision
M1 Charter approved	27 Mar 2026	Initiation closed, design authorised
M2 Design signed off	15 May 2026	Build authorised
M3 Build complete	28 Aug 2026	Testing authorised
M4 EPBCS go/no-go	9 Oct 2026	Training and cutover authorised
M5 EPBCS go-live	2 Nov 2026	FY27 budget launched in EPBCS
M6 FCCS go-live	8 Jan 2027	Year-end close in FCCS

7. Tolerances

The steering committee delegates day-to-day management to the project manager within these tolerances. If a forecast goes beyond one of them, the project manager raises an exception report and the committee decides.

Area	Tolerance	Escalation
Time	±10 working days on each go-live date	Exception report to the steering committee
Cost	+5 % of the authorised budget (about 24 k€ on 480 k€)	Exception report; contingency released only through a change request

Area	Tolerance	Escalation
Scope	All Must requirements delivered; Could items may be deferred by the board	Change request
Quality	UAT exit criteria (section 10)	No go-live without them, or a documented board decision
Risk	Any risk scoring 20 or more	Escalated to the sponsor within 48 hours

8. Project controls

Control	Frequency	Participants	Output
Steering committee	Monthly and at each stage end	Project board, project manager	Decisions, highlight report, end stage report
Project committee	Weekly	Project manager, leads, key users	Checkpoint, RAID review
Stand-up	Daily in build and testing	Project team	Blockers, defect triage
Exception report	When a tolerance is forecast to be exceeded	Project manager to the board	Options and recommendation

Change control

- Every request affecting scope, cost or dates is logged in the change log, costed and assessed.
- The project manager approves requests up to 10 k€ with no effect on a go-live date.
- Above that, or when a go-live moves, the steering committee decides.
- The 48 k€ contingency is released only through approved change requests; the authorised budget is updated accordingly.

9. Risk management approach

Score	Probability (P)	Impact (I)
1	Rare (under 10 %)	Negligible: absorbed within the stage
2	Unlikely (10 to 30 %)	Minor: a few days or under 5 k€
3	Possible (30 to 50 %)	Moderate: a week, or 5 to 15 k€
4	Likely (50 to 80 %)	Major: threatens a milestone or 15 to 30 k€
5	Almost certain (over 80 %)	Severe: a go-live date or over 30 k€

The risk score is P × I. One scale applies to every report: **low** from 1 to 7, **medium** from 8 to 14, **high** from 15, and a score of 20 or more blocks a go-live. Each risk has an owner and one of the PRINCE2 responses: avoid, reduce, fallback, transfer, share or accept. The register is reviewed weekly and presented monthly to the steering committee.

ID	Initial risk	P	I	Score	Owner	Response
R1	Poor quality of historical ERP data	4	4	16	IT	Reduce: cleansing, monthly reconciliation
R2	Key users unavailable during testing (budget season)	4	3	12	Sponsor	Reduce: test calendar agreed by the CFO
R3	Delay in the ERP data flows	3	4	12	IT	Fallback: manual file loads
R4	Complex consolidation rules (NCI, FX)	2	4	8	Consol.	Reduce: dedicated tests, auditor review
R5	Resistance to change (Excel habits)	3	3	9	PM	Reduce: champions, demos, hands-on training
R8	Project budget overrun	3	3	9	PM	Reduce: monthly earned value, scope trade-offs

10. Quality management approach

Test stage	Who	Purpose
Configuration tests	Consultants	Each form, rule and report works as designed
System integration testing (SIT)	Consultants, IT	End-to-end flows from the ERP to the reports
User acceptance testing (UAT)	Key users	Real processes replayed in the tool, against the requirements
Performance and security	IT, consultants	Response times; access restricted by entity
Parallel run (FCCS)	Consolidation team	November close run in both Excel and FCCS, results reconciled
Regression	Key users	After each Oracle monthly update, before production

UAT exit criteria and defect severity

- 100 % of test cases executed; at least 95 % passed; 100 % of security tests passed.
- No critical defect open; no more than two major defects, each with a documented workaround.
- **Critical**: a process cannot be completed or figures are wrong, with no workaround.
- **Major**: a process is impaired but a workaround exists. **Minor**: cosmetic or low impact.

11. Communication plan

Audience	Message	Channel	Frequency	Owner
Project board	Status, decisions needed, tolerances	Steering committee	Monthly	Project manager
Finance teams	What changes, when, what is expected of them	Newsletter, demos	Each stage	Sponsor, PM
Key users	Test calendar, defects, training	Project committee	Weekly	Project manager

Audience	Message	Channel	Frequency	Owner
Subsidiary controllers	Consolidation packages and calendar	Webinar, user guides	Before each close	Consolidation team
IT and ERP team	Data flows, environments, Oracle updates	Technical meeting	Fortnightly	IT and ERP lead

Authorisation

The steering committee approved this document on 27 March 2026 (milestone M1, decision DC1). The initiation stage is closed and the design stage is authorised. This document is the baseline against which later changes are assessed.
